


Act ID	Activity Description	Plan Dur	Start	Finish	Latp Start	Latp Finish	Latp Total	Flow	Start	Finish	Latp Start	Latp Finish	Latp Total	Flow
S55220	S122-23	17	09 JUN 09	27 JUN 09	09 JUN 09	27 JUN 09	12 JUN 09	0						
S55230	S112-113	14	29 JUN 09	14 JUL 09	29 JUN 09	14 JUL 09	14 JUL 09	0						
S57-560	Inspection Pit / Liaison with UU / UU Diverston													
CM5855	S37-36	14	15 JUL 08	30 JUL 08	15 JUL 08	30 JUL 08	30 JUL 08	0						
CM5866	S37-38	12	21 JUL 08	13 AUG 08	21 JUL 08	13 AUG 08	13 AUG 08	0						
CM5870	S38-39	12	14 AUG 08	26 AUG 08	14 AUG 08	26 AUG 08	26 AUG 08	0						
CM5880	S38-40	12	28 AUG 08	10 SEP 08	28 AUG 08	10 SEP 08	10 SEP 08	0						
CM5890	S40-167	12	11 SEP 08	24 SEP 08	11 SEP 08	24 SEP 08	24 SEP 08	0						
CM5900	S167-168	12	25 SEP 08	08 OCT 08	25 SEP 08	08 OCT 08	08 OCT 08	0						
CM5910	S168-171	12	09 OCT 08	22 OCT 08	09 OCT 08	22 OCT 08	22 OCT 08	0						
CM5920	S141-42	12	23 OCT 08	05 NOV 08	23 OCT 08	05 NOV 08	05 NOV 08	0						
CM5930	S42-43	12	06 NOV 08	19 NOV 08	06 NOV 08	19 NOV 08	19 NOV 08	0						
CM5940	S40-44	12	20 NOV 08	03 DEC 08	20 NOV 08	03 DEC 08	03 DEC 08	0						
CM5950	S44-45	12	04 DEC 08	17 DEC 08	04 DEC 08	17 DEC 08	17 DEC 08	0						
CM5960	S45-46	12	18 DEC 08	31 DEC 08	18 DEC 08	31 DEC 08	31 DEC 08	0						
CM5970	S46-171	12	02 JAN 09	15 JAN 09	02 JAN 09	15 JAN 09	15 JAN 09	0						
CM5980	S171-50	12	16 JAN 09	02 FEB 09	16 JAN 09	02 FEB 09	02 FEB 09	0						
CM5985	S50-51	32	03 FEB 09	11 MAR 09	03 FEB 09	11 MAR 09	11 MAR 09	0						
CM5988	S51-52	21	12 MAR 09	06 APR 09	12 MAR 09	06 APR 09	06 APR 09	0						
CM5993	S52-53	21	07 APR 09	07 APR 09	07 APR 09	07 APR 09	07 APR 09	0						
CM5994	S54-55	21	07 MAY 09	02 JUN 09	07 MAY 09	02 JUN 09	02 JUN 09	0						
CM5998	S54-55	12	03 JUN 09	16 JUN 09	03 JUN 09	16 JUN 09	16 JUN 09	0						
CM6000	S55-56	12	17 JUN 09	30 JUN 09	17 JUN 09	30 JUN 09	30 JUN 09	0						
CM6010	S56-60	12	01 JUL 09	14 JUL 09	01 JUL 09	14 JUL 09	14 JUL 09	0						
S57-590	Clearance of Squattered Huts													
CM6068	S57-169	57	15 JUL 08	18 SEP 08	15 JUL 08	18 SEP 08	18 SEP 08	0						
CM6070	S57-170	21	14 OCT 08	05 NOV 08	14 OCT 08	05 NOV 08	05 NOV 08	0						
CM6090	S170-58	20	07 NOV 08	28 NOV 08	07 NOV 08	28 NOV 08	28 NOV 08	0						
CM6100	S58-59	21	01 DEC 08	24 DEC 08	01 DEC 08	24 DEC 08	24 DEC 08	0						
CM6110	S59-60	30	26 DEC 08	02 FEB 09	26 DEC 08	02 FEB 09	02 FEB 09	0						
S56-563	S36A-S36B (Trenchless)													
CM6209	S36A-S36B (Trenchless)	14	01 SEP 08	16 SEP 08	01 SEP 08	16 SEP 08	16 SEP 08	0						
CM6210	S36A-S36B (Trenchless)	30	17 SEP 08	21 OCT 08	17 SEP 08	21 OCT 08	21 OCT 08	0						
CM6212	S36A-S36B (Trenchless)	48	22 OCT 08	16 DEC 08	22 OCT 08	16 DEC 08	16 DEC 08	0						
CM6220	S36A-S36B (Trenchless)	17	17 DEC 08	12 MAR 09	17 DEC 08	12 MAR 09	12 MAR 09	0						
CM6270	S36A-S36B (Trenchless)	21	13 MAR 09	07 APR 09	13 MAR 09	07 APR 09	07 APR 09	0						
CM6280	S36A-S36B (Trenchless)	48	08 APR 09	04 NOV 09	08 APR 09	04 NOV 09	04 NOV 09	0						
S64-S70	Trenchless													
CM6226	S64-S70 (Trenchless)	14	13 MAR 09	28 MAR 09	13 MAR 09	28 MAR 09	28 MAR 09	0						
CM6230	S64-S70 (Trenchless)	21	30 MAR 09	27 APR 09	30 MAR 09	27 APR 09	27 APR 09	0						
CM6240	S64-S70 (Trenchless)	140	28 APR 09	14 OCT 09	28 APR 09	14 OCT 09	14 OCT 09	0						
CM6250	S64-S70 (Trenchless)	21	15 OCT 09	09 NOV 09	15 OCT 09	09 NOV 09	09 NOV 09	0						
CM6300	S64-S70 (Trenchless)	43	10 NOV 09	31 DEC 09	10 NOV 09	31 DEC 09	31 DEC 09	0						
S110-S132	S127-S133													
S54975	Inspection Pit / Liaison with UU / UU Diverston	30	01 DEC 08	05 JAN 09	01 DEC 08	05 JAN 09	05 JAN 09	0						
S54980	S110-111	14	08 JAN 09	31 JAN 09	08 JAN 09	31 JAN 09	31 JAN 09	0						
S54990	S111-113	14	22 JAN 09	10 FEB 09	22 JAN 09	10 FEB 09	10 FEB 09	0						
S55010	S113-114	14	17 FEB 09	28 FEB 09	17 FEB 09	28 FEB 09	28 FEB 09	0						
S55020	S114-121	14	27 FEB 09	14 MAR 09	27 FEB 09	14 MAR 09	14 MAR 09	0						
S55030	S123-124	14	16 MAR 09	31 MAR 09	16 MAR 09	31 MAR 09	31 MAR 09	0						
S55040	S124-125	14	01 APR 09	21 APR 09	01 APR 09	21 APR 09	21 APR 09	0						
S55050	S125-132	14	22 APR 09	09 MAY 09	22 APR 09	09 MAY 09	09 MAY 09	0						
S55060	S126-128	14	11 MAY 09	26 MAY 09	11 MAY 09	26 MAY 09	26 MAY 09	0						
S55070	S127-128	14	27 MAY 09	13 JUN 09	27 MAY 09	13 JUN 09	13 JUN 09	0						
S55080	S128-131	14	16 JUN 09	30 JUN 09	16 JUN 09	30 JUN 09	30 JUN 09	0						
S55090	S129-130	14	01 JUL 09	16 JUL 09	01 JUL 09	16 JUL 09	16 JUL 09	0						
S55100	S130-131	14	17 JUL 09	01 AUG 09	17 JUL 09	01 AUG 09	01 AUG 09	0						
S55110	S131-132	14	03 AUG 09	18 AUG 09	03 AUG 09	18 AUG 09	18 AUG 09	0						
S47-S50	Inspection Pit / Liaison with UU / UU Diverston													
AW6260	S47-172	17	11 JAN 10	29 JAN 10	11 JAN 10	29 JAN 10	29 JAN 10	0						
AW6270	S47-173	9	30 JAN 10	09 FEB 10	30 JAN 10	09 FEB 10	09 FEB 10	0						
AW6280	S172-173	7	10 FEB 10	17 FEB 10	10 FEB 10	17 FEB 10	17 FEB 10	0						
AW6290	S173-149	7	18 FEB 10	25 FEB 10	18 FEB 10	25 FEB 10	25 FEB 10	0						
AW6300	S48-49	7	26 FEB 10	05 MAR 10	26 FEB 10	05 MAR 10	05 MAR 10	0						
AW6310	S49-50	10	05 MAR 10	17 MAR 10	05 MAR 10	17 MAR 10	17 MAR 10	0						
S16-S36														

Start Date 31 JAN 08
 Finish Date 19 APR 10

Page : 8A

DC/2007/18
 Yung Shue Wan and Sok Kwu Wan Village Sewerage, Stage 1 Works
 Project Programme Rev. 4

Date	Revision	Checked	Approved
02 MAY 08	Revision 1	SIL	KYS
16 JUN 08	Revision 2	SIL	KYS
03 SEP 08	Revision 3	SIL	KYS
31 OCT 08	Revision 4	SIL	KYS

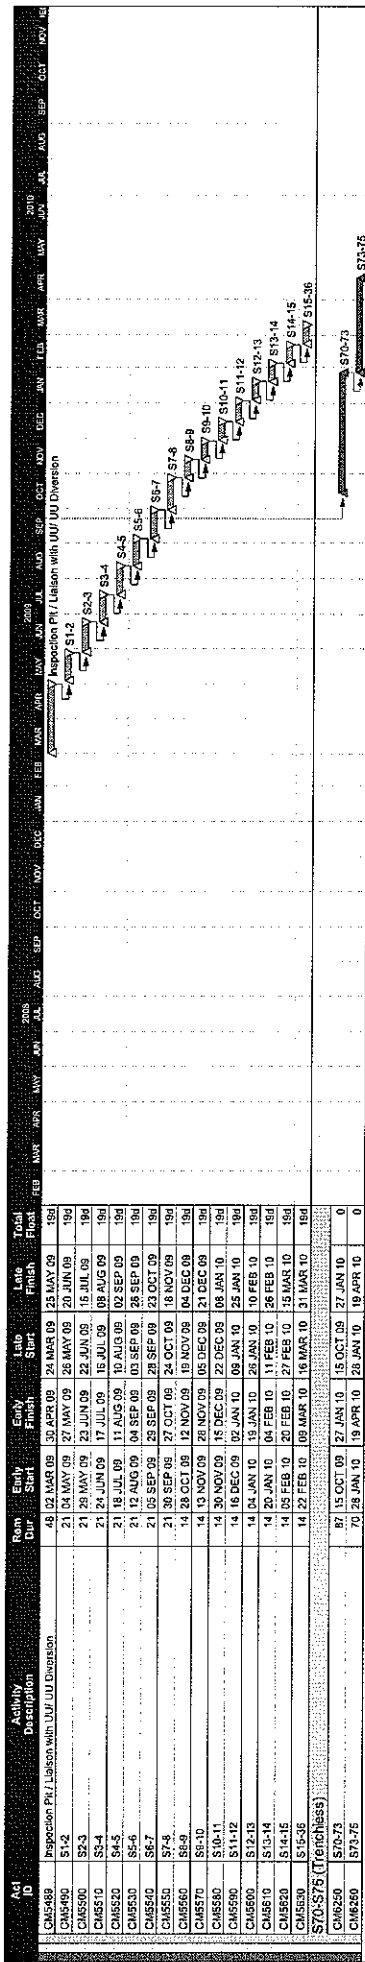

Revision	Date	Checked	Approved
Revision 1	02 MAY 08	SL	KYS
Revision 2	16 JUN 08	SL	KYS
Revision 3	03 SEP 08	SL	KC
Revision 4	31 OCT 08	SL	KYS

DC/2007/18
Yung Shue Wan and Sok Kwo Wan Village Sewerage, Stage 1 Works
Project Programme Rev. 4

Start Date: 31 JAN 08
Finish Date: 19 APR 10

Page: 10A
